TRACERA

State & Forward Docket

tracera-state-forward-20261017-q1

Evidence-bound full-state baseline and forward execution path

Unified intent accepted; full product acceptance NOT ESTABLISHED.

Candidate 3fd3310fb98fdd2f9bca99eddd669f974fb1fb61

Baseline ae68aea7febd772282606bf1e142d507316cfea0

Generated 2026-10-17T09:39:28.530213+00:00

Owner: Instinct / Tracera. Source PR1157 is open and unmerged. No production promotion. Screenshots and recordings were not used.

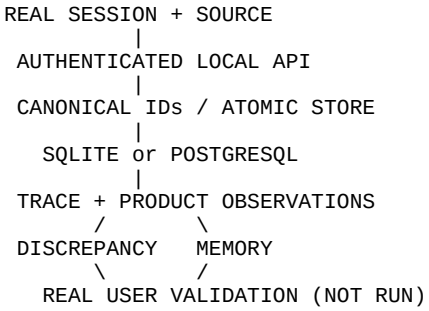

Two-minute cockpit

Tracera is an original owned project, with accepted unified intent: local-first trace/session linking, memory distillation and audit replay plus persistent product modelling and discrepancy discovery. Q1 delivered a real durable product-observation API, detector identity corrections, SQLite/PostgreSQL atomicity and a restart/replay runtime journey. Full unified CVP and real user acceptance remain unproved. Source PR1157 is open; no merge or production promotion.

Axis	Current qualified statement
Implementation	3 narrow Q1 checkpoints implemented
Engineering	Selected tests and review passed
Usable journey	1 synthetic local API/restart journey
User validation	No actual acceptance receipt

NEXT: connect an actual producer/session to the durable semantic model, then qualify trace-to-discrepancy-to-memory with restart, foreign-product negatives and a real beneficiary.

Intent and source authority

Direct user requirements: complete API/frontend gap inventory, named artifact fidelity, complete data, CIVIS zero-item note, read-only original audit then explicit authorized implementation, preserved checkouts and no merges. Registry at05e1638 defines local-first trace/session dependency reasoning, memory distillation and audit replay. Its CVP also includes desktop. docs5 explicitly calls its persistent product-model program proposed; it is not authority to erase Registry identity. Draft WP07 is a design proposal, not accepted wholesale. Preserve contradiction for user decision. UPDATE2026-10-17T09:22:59Z: user explicitly chose BOTH with unified scope. This supersedes the unresolved authority question; preserves both branches and adds a missing integration obligation. No implementation credit is earned by changing the scope denominator.

Actual usability today

Q0 exactmain ae68 was built and exercised in an isolated Windows SQLite runtime: readiness, valid issue ingest, persisted Story after restart; empty ingest422 and pagination400/missing404. That proves this limited API path, not full product semantic import or trace-memory CVP. Historical deployed ports8080/8091 were later refused; current public path behind Access was not qualified. No current GUI, desktop installation, release or actual beneficiary acceptance is claimed. Q1 now additionally proves actual candidate binary47a7a5bba1eaff02264b6c338ee0d748312c83b8012cd3b1d4512f91656e0daf on owned loopback19147: typed batch200, persisted read200, real freshness detector finding200 referencing observation, foreign product404, restart exact read equality, replay200 accepted0/replayedtrue. Owned processes stopped. This is a synthetic local API journey, not an actual external producer or user session.

Architecture and data flow

Agents/session and external source adapters -> Axum authenticated routes -> Store -> SQLite or PostgreSQL. Canonical Items, Story/Evidence/TraceLink and SWEE graph are distinct models. Product semantic observations add product/baseline/capability/source scope in Q1. Frontend projections and two MCP packages may expose different entrypoints; no proof yet all share one coherent beneficiary model. Memory distiller currently owns Vec state and Instant in process; source presence is not durable cross-session API acceptance.

CVP and MVP boundary

Registry identity-preserving CVP: one user/machine/durable workspace captures a real session, queries cross-run spec dependency, distills memory consumed by next session, and survives restart locally; desktop primary nondeveloper install surface retained. docs5 candidate CVP: real owned product import, genuine source-backed discrepancy, bounded navigation, sourcechange/restart. Both are now explicitly unified by the user decision. An appropriate MVP adds only agreed retained authoring/typed views and safe local delivery around the selected CVP; it cannot be declared merely because Q1 batch persistence passes. Unified bridge acceptance: capture actual authorized session/run with stable product, capability, baseline and source IDs; persist causal links; explain a genuine discrepancy and affected sessions/capabilities; derive attributable memory consumed next session; reconcile source changes and restart without duplication/leakage. This bridge is not yet qualified.

Four independent progress axes

Raw implementation: Q1 code/checkpoints reported in candidate receipts. Verified engineering: exact selected SQLite/PG/router/detector tests and independent review only. Complete usable journeys: Q0 limited API import/reopen; no full identity-preserving CVP yet. Real user validation/value: no receipt, unknown total denominator and no earned acceptance. Full-product numeric progress is undefined; all four numerator/denominator values null until accepted nonoverlapping baseline is locked. Q1 selected raw implementation checkpoints3/3 (identity/durability/mounted API); engineering scope qualified by17detector,96library,121binary,4existingDB,5newSQLite and1explicit PostgreSQL tests, strict clippy/fmt/diff. One bounded independent reviewer inspected actual code/logs, did not rerun suite. One local synthetic API journey succeeded; zero actual user-validation receipts. These selected counts are not full-product numerators.

Historical evidence and drift

Prior audit29issues +44view rows =73inventory rows;7baselines652promise records;284frontend method/reference rows. Those denominators overlap semantically and are not percentages of current product completion. Historical TRACERA533items and CIVIS0 were genuine nonstub observations. Earlier43stub200responses among57GETprobes describe old deployment. New source honest501 is improvement in truthfulness, not implementation of missing feature. Old code-count estimates240+60+10 were overlapping and are superseded by bounded unique literal census, not summed.

Testing and adversarial explanation

Positive fixture proof must be paired with foreign product/capability/baseline/source, malformed IDs, replay conflict, concurrent identical replay, late rollback and reopened persistent state. Alternative explanation: empty result may be legitimate zero rather than stub; use nonstub Store path and source counts. A501 may be honest missing capability rather than regression. Unit detector pass may hide unmounted data path; require router/database journey. Current owner logs are originating evidence, independent review is separate but does not count as rerunning tests. Fullsuite exposed stale reprobe threshold>=48 while base root literal list had35; fix-forward exact35 retained route assertions and explicit unknown404, not feature tests. Original RED and final GREEN both preserved in owner receipts. Isolated per-route reprobes do not prove all mounted routes.

Security privacy and integrity

Loopback-only trusted singleoperator is materially different from multiuser hosted deployment. Shared bearer does not establish perproject authorization. Selfhost docs explicitly warn forward-auth placeholder is not public protection. Preserve failclosed gates; no policy bypass. Need privateevidence export controls, untrustedprose/data injection tests, principal/projectnegativecases, payloadbounds, restoreintegrity. Hashes prove byteidentity not truthful claims/authorship. No credentials are included in this dossier.

UX AX DX and documentation

Historical sidebar44rows had40project links gated by ProjectNotFound and3typed detailIDs unavailable. These are stale observations requiring current requalification. Source ApiView advertises project/item writes inconsistent with unavailable server paths: make status generated from a real capability contract. Keyboard focus, screenreader labels, loading/errors/trueempty and largepagination remain unqualified. Current RustCLI stack management is not historical Typer fullCRUD parity; historical matrix explicitly labels retired Python stack. New independent source review: packaged desktop defaults external rich gateway18000 and only explicit legacy override starts Compose; standalone install/runtime not qualified. Desktop/main.js defaults hosted endpoint while frontend desktop target defaults loopback; choose supported shell. Dormant updater declares signature/publicKey but checked download path validates SHA only and no streaming cap; module unimported, so not a mounted exploit. Activate only with authenticity/stream limits and negative tests.

Lineage rewrite and migration

GitHub prior metadata says original project fork=false,parent=null; oldtracertm name does not imply external upstream fork. Do not invent upstream divergence requirements. Python->Rust transition and multiple desktop/MCP surfaces do require retainedbehavior/data/consumer parity and explicit retirement decisions. Snapshot import and Q1typedbatch do not prove all historic data migrated; preserve durable records and rehearse update/rollback without history rewrite.

Research alternatives and discriminating pilot

docs5 shortlist manualGit/search, Backstagecatalog, StrictDoc, SCIP/LSPdependencysearch and hotspotanalysis remains a hypothesis ledger, not verified current comparisons. No unsupported superiority or cost claims. First compare exact owned seededgap task under matched input revisions and separate idiomatic alternatives; record missingdynamicrelationships, staleevidence, falsepositive/negative, time/interventions/privacy and maintenance costs. Reuse localDB/nativeindex/testreports before customengines where actual consumer outcome permits.

Tracking and operations

Actual AgilePlus wrapper absent and local8765 connection failed in bounded collector. Engine state UNKNOWN, no invented feature/WP IDs; this dossier is an assessment snapshot, not competing taskregistry. Existing heartbeat sunsetblocked after unchangedexternalblocker ticks; no claim new scheduler installed. No paidCI, productionrestart, deploymentpromotion or merge occurred. Actual cloudmonthlycost unknown; local64GiBWindows compute suitable heavierbuilds, localmac selected smallPDF/schema work.

Forward path and dependencies

The accepted unified identity requires a detailed nonoverlapping obligation baseline before mature-completion scoring. Q1verifiedcandidate -> independentreview -> localrealadapterjourney -> canonical project/source/linkidentity -> selectedCVP ingest/query/memory or discrepancy UI -> freshinstall/restore -> actualuserfeedback -> retainedparityclosure. Integrate exactcandidate before claiming deployedbehavior. Parallelize nonoverlap frontendartifactfidelity, trace-memory wiring and assurance; sharedStore/schema owners serialize integration.

Estimates and calibration

Planning ranges are expert scenarios, not statisticalP50/P90. Comparableaccepted fullCVP sample size0; observedQ1 narrowed contract work and Q0 isolatedbuild are different work classes. Next30m: validate candidate targeted gates and consolidate exactreceipt;1h: reviewedcodePR plus generateddocket publication if hooks pass;4h: one realownedadapter dataset through scopedpersist/read/detector path and truthful UI/APIstatus;24h: exercise selectedlocalCVP integration or expose preciseblockeddependency, plus restore/errorcontrols. Humanintentdecision and realuserfeedback are externalwaiting, not agentcoding effort. Actual narrowed Q1 delivery ~24minutes versus prior25minute estimate is one sample of narrowly scoped engineering output, not accepted fullCVP calibration. Next milestones are measured from this snapshot, not promises of user acceptance.

CVP and mature completion scenarios

Productmodel candidateCVP remaining24-44engineeringdays from prior audit is lowconfidence and may shrink materially with scoped acceptance; trace-memoryCVP has not been decomposed/estimated sufficiently, so time unknown until next4h mapping. At constrained2seniorowners+agents effective1.2-1.5engdays/workday, former scenario roughly4-8workweeks, not a commitment. Full retainedv1 prior95-215engineeringdays is provisional lower/likely/high planning spread, not ceiling; unresolved disposition of the 652 historical promise records prevents maturecompletion forecast. Do not divide by nominalagentcount or pretend everyunknown is scaling.

Operating cost resources and rework

No new paidresource authorized or spent by this doclane. PDF/schema smalllocalCPU job; heavyRustWindows placement available. Actual computehours, hostingbill, bandwidth, storagegrowth and maintenancecost not measured. Budget planning: reserve20-40percent of scoped implementation effort for integration/negativecontrols/rework until comparableoutcomes qualify; this is explicit uncalibrated planning allowance, not observedrate. Reviewqueue and externalfeedback add walltime independently.

Decisions risks and stop conditions

D01 unified identity accepted: retain both goal branches; retire nothing without explicit authority. D02no merge/deploy without exactauthorization. D03keep historicalevidence immutable; correctionappend rather than rewrite. R01crossproduct/namespacecollision highimpact; typedbatch isolationcontrols. R02silentemptyhealth highimpact; explicit unavailable/unknown. R03privateevidence publicleak critical; export/authorizationnegativecontrols. R04staleevidence medium/high; sourceboundfreshness. Stop promotion on lossidentity, dataownership, privacy, atomicity or failclosedauth; continuedocs alone never closes product.

Publication and closeout

Canonical typedrecords and frozeninputs generate MarkdownHTMLPDFCSV; schema validator is structural only. Sourceandoutputhashes bind snapshot, evaluator and renderer. NewdocPR is separate from sourcecandidate and audit1132. Registry pointer must reference actual productcommit and samePDFhash afterremoteverification. Safari command success proves launchrequest, not that user read or acceptedPDF. Every remote outcome remains explicit until verified; localfile/openPR/merged/installed/accepted are separate states.

Coverage matrix and explicit uninspected frontier

Intent: actual Registry intent/CVP/boundary, docs5 dossier, README and WP07 inspected; full historic conversation archive and1963commit history NOT reinspected. Implementation: source baseline architecture, governance, memory state, unavailable route families and prior bounded audit inspected; all functions/optional build profiles NOT examined. Frontend: all63tracked route filenames and955lexical API candidate lines enumerated, not all journeys executed. Explicit family census197unique literals excludes direct router, mixed/dynamic registrations and fallback, so differs from earlier216/39module census and is not additive. Assurance: Q1 owner tests and one independent bounded review, no numeric wholeproduct coverage or new AX/browser/user tests. Deployment: Q0 isolated receipt and historic unavailable deployed path, no current production qualification. Releases/cost/adoption: NOT inspected or unmeasured. Research: shortlist from proposed dossier, no new comparative pilot. These limits are coverage gaps, not passes.

Goal and obligation drill-down

25 reconstructed branches; no claim that all historical intent or all implementation paths have been inspected. Each source location is bound to the baseline unless the Q1 receipt explicitly names the candidate.

G01 Authority and mature identity

Direct user accepted explicitly unified trace/session/memory/audit and product/discrepancy scope at2026-10-17T09:22:59Z.

Present state: PASS; review PROPOSED

Exact source: inputs/registry-intent.md; inputs/registry-cvp.md; inputs/docs5-DOSSIER.md

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Owning intent records retain both and define identity-preserving bridge acceptance; no retrospective feature acceptance.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: none defined; effort: Unestimated pending exact retained scope

G02 Local trace capture

Capture real input/tool/output session to durable local workspace with source/spec/session identifiers.

Present state: UNKNOWN; review PROPOSED

Exact source: README.md; crates/tracera-server/src/router.rs:153-173

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Real session capture, exact count/content after restart; invalid/foreign/dangling edges rejected.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G03 Cross-run dependency reasoning

Answer affected prior sessions when a spec changes, using persisted trace graph.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/handlers/governance.rs:9-45

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Seed known dependency plus unrelated session; persisted query yields exact affected set after reopen. Supplied-links computation alone insufficient.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G04 Memory distillation

Distill lastN real sessions into stable memory consumable by next session with provenance and privacy.

Present state: FAIL; review PROPOSED

Exact source: crates/tracera-server/src/memory/distillation/distiller.rs:12-26

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Persist memory, link source sessions and serve real consumer; restart restores same accepted entry; private/untrusted input cannot escape into public projection.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G05 Audit and evidence replay

Reproduce who ran what/when per workspace; evidence freshness and integrity explicit.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/handlers/evidence.rs

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Real evidence/source/run timestamps survive restart, altered/missing/stale evidence fails honestly; audit export replay verified.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G06 Product semantic model

Durable typed product observations now verified at3fd3310; full actual-product discrepancy UI remains unfinished.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/product/; docs/WP-07-product-graph-design.md (DRAFT)

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Real owned product import and independently adjudicated gap; no cross-product/baseline/capability leakage; source change invalidates affected evidence.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G07 Import and canonical identity

Sources, products and namespaces preserved across replay, partial failure and complete pagination.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/ingest/persist.rs:39-107

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Two sources same externalID stay distinct; retry idempotent; late error atomic or explicit recoverable partial contract. Q1 product batch does not automatically repair Story importer.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G08 Project catalog and CIVIS

All owned projects have stable identity; CIVIS genuine zero items distinct from absent/unavailable.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/pg_store/projects.rs; historical audit

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Item-only and empty project load correctly; all pages complete; failure never reported as empty.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G09 Named artifact fidelity

Every named view X renders only complete artifact X, correct project/type and detail fields.

Present state: UNKNOWN; review PROPOSED

Exact source: frontend/apps/web/src/pages/projects/views/;
inputs/TRACERA-HISTORICAL-VIEW-COVERAGE.csv

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Click every required sidebar/view and representative typed detail using real IDs; 44 historical rows require current requalification.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G10 Specifications Hub

Real ADR/contract/feature/scenario aggregates plus honest health/evidence denominator.

Present state: FAIL; review PROPOSED

Exact source: crates/tracera-server/src/routes/specs.rs; frontend SpecificationDashboard.tsx

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Summary shape matches summary-hooks; totals reconcile complete typed collections; missing compliance/pass data null; failures distinct from zero.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G11 Authoring and links

Accepted project/item editing and intent->code->test/evidence linking durable and authorized.

Present state: FAIL; review PROPOSED

Exact source: crates/tracera-server/src/handlers/projects.rs; routes/links.rs

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Actual scoped CRUD and links survive restart; invalid/cross-project updates rejected; UI cannot advertise unavailable methods as implemented.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G12 Bounded search and exploration

Explainable bounded navigation, explicit truncation/unsupported dynamic relationships.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/routes/graph.rs; routes/search.rs

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Known source anchor found; bounded query terminates cycles and marks truncation; no fabricated edge or silently missing page.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G13 Native test/result integration

Distinguish test definitions, execution, results and freshness.

Present state: FAIL; review PROPOSED

Exact source: crates/tracera-server/src/routes/test_runs.rs; routes/spec_analytics.rs

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Ingest actual native report, preserve failed cases/denominators and source revision; unsupported execution honest unavailable.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G14 API CLI MCP parity

Current Rust interfaces share canonical data and errors; historical Python oracle not mistaken for current implementation.

Present state: UNKNOWN; review PROPOSED

Exact source: Cargo.toml; crates/tracera-cli/; crates/tracera-mcp/; crates/tracertm-mcp/

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: One real supported operation roundtrips same IDs across required interfaces; unsupported declared; demo modes excluded from acceptance.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G15 Authentication privacy isolation

Trusted single-user local boundary explicit; shared URL protected; secrets and evidence remain private.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/auth.rs; router.rs; deploy/selfhost/README.md

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: 401 missing credential,403/404foreign scope, no public backend bypass, redacted logs/export, payload limits and hostile prose tests.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: none defined; effort: Unestimated pending exact retained scope

G16 Durability recovery migration

SQLite/PG durable accepted models, backup/restore, upgrade/cutover with original records preserved.

Present state: UNKNOWN; review PROPOSED

Exact source: crates/tracera-server/src/db.rs; migrations-*; Q0/Q1 receipts

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Real persistent reopen plus crash/backup/restore/migration trial; compare IDs/content beforeafter; old/new data contract explicit.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: none defined; effort: Unestimated pending exact retained scope

G17 Install and desktop delivery

Real local server+web and packaged nondeveloper desktop, update/recovery under accepted platform boundary.

Present state: UNKNOWN; review PROPOSED

Exact source: desktop/README.md; crates/tracera-tauri/; docs/ARCHITECTURE.md

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Fresh install useful journey, local-first no mandatory remote API, update retains data and recoverable previous artifact.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G18 Deployment artifact provenance

SourceSHA->binaryhash->configuration->database->reachable URL attested.

Present state: UNKNOWN; review PROPOSED

Exact source: inputs/TRACERA-Q0-RUNTIME-QUALIFICATION.md

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Current hosted and installed artifact exact identity, authenticated real path; Q0 isolated readiness does not qualify production.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G19 UX accessibility and DX

Keyboard navigation, accessible errors/loading/empty states, fresh-start docs and truthful API capability labels.

Present state: UNKNOWN; review PROPOSED

Exact source: frontend/apps/web/src/pages/projects/views/ApiView.tsx; frontend/apps/web/src/routes/

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Keyboard/focus/labels/contrast assistive audit without captures; no mock data presented as real; documented command starts actual profile.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G20 Assurance and security gates

Meaningful positive/negative integration, critical coverage, no masked gates, dependency threats assessed.

Present state: UNKNOWN; review PROPOSED

Exact source: .github/workflows/coverage.yml; lefthook.yml; frontend/apps/web/vitest.config.ts

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Run required local gates with explicit coverage denominator/floor; deliberate regression fails; masked Ruff/Python collection fixed if retained.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: none defined; effort: Unestimated pending exact retained scope

G21 Research and alternatives

Test reuse/retain/adopt hypothesis against real beneficiary task, not marketing superiority.

Present state: NOT_RUN; review PROPOSED

Exact source: inputs/docs5-DOSSIER.md:comparators

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Version-pin manualworkflow, catalog/search, requirements/source links and dependency exploration peers; matched seeded cases plus idiomatic comparisons.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G22 Operations and economic ownership

Owned startup/shutdown, logs, backup schedule, cost/resource boundary and sunset owner.

Present state: UNKNOWN; review PROPOSED

Exact source: docs/04-guides/DEPLOYMENT_GUIDE.md; prior heartbeat ledger

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Restore rehearsal, dependency failure, resource bounds and explicit recurring-job owner; no billed services added; actual hosting cost unknown.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G23 Actual beneficiary acceptance

Real user completes useful identity-preserving journey and confirms value.

Present state: NOT_RUN; review PROPOSED

Exact source: No actual user-session/feedback receipt supplied

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Unfamiliar authorized user real owned input, recorded task outcome/interventions/feedback, failures retained; fixture pass does not qualify.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G24 Full historical parity disposition

Retain652 baseline promise records and29historical gaps without treating overlaps as accepted scope or closure.

Present state: UNKNOWN; review PROPOSED

Exact source: inputs/TRACERA-BASELINE-PROMISES.csv; inputs/TRACERA-GAP-INVENTORY.csv

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Each retained promise maps accepted goal/current contract/closure proof, or explicit authority for supersession/defer/retire; no silent sunset.

Negative oracle: Foreign scope/stale/missing/failed dependency must fail honestly; no fabricated success

Owner: Tracera product owner; dependencies: G01; effort: Unestimated pending exact retained scope

G25 Unified trace-to-product evidence bridge

Actual session/run -> source/product/capability observations -> discrepancy and affected dependencies -> attributable durable memory consumed next session.

Present state: UNKNOWN; review PROPOSED

Exact source: README.md; router.rs codex session endpoints; Q1 product observations API

Consequence: beneficiary cannot rely on this full goal until its closure oracle is exercised.

Closure / positive oracle: Real authorized producer and source anchor, semantic causal navigation, exact restart/replay equality and foreign-product negative controls; meaningful actual user outcome.

Negative oracle: Foreign product/baseline/source cannot gain evidence credit; malformed replay rejected atomically

Owner: Tracera implementation owner; dependencies: G02, G03, G04, G06, G07, G15, G16; effort: First4h decomposition; full duration uncalibrated

Source coverage and limits

inputs/sfd/CONTRACT.md

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: ff61a6386e16d29bc094940c2f63f0ba5003bc53ae0f2f727702574b37352a84

governing contract

inputs/sfd/ADOPTION.md

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: 933b4131fd56df20bf54c2ad86170548c1b15a6061817b43db1a3d0dc22af5c5

governing contract

inputs/sfd/schemas/snapshot.schema.json

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: 44bce147ba86eb756825000833dd880490a2208547ccd347befc1d2e15e0c83a

governing contract

inputs/sfd/tools/sfd.py

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: 86a0702ebf75b51e4e0860d259a6a01590dca3b738ee9438b66b5fc9cd48b5fd

governing contract

inputs/registry-intent.md

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: 75e1712da2809f2fbf9a33c6ad03c55af4b84a68c80879e9b11a30490419f5fd

intent authority; historical runtime statements not current proof

inputs/registry-cvp.md

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: d8990737c3e6b1176779c9276556bb16cd2fbe26badb5669cf127c8593184df3

intent authority; historical runtime statements not current proof

inputs/registry-boundary.md

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: 1d9f1d502a451f3f0ccfe10ecd025c7e0b8ea1a8506ccb9ad40742995f93be7b

intent authority; historical runtime statements not current proof

inputs/MASTER-ASSESSMENT-KIT.md

Revision: 05e163820f1a207f2f827a5485ce6ca04084107f; SHA256: c72c7173d0824cb0f4d175c07b0b4a7722ab9244b4d0facc9eb48e4da3b5cd84

assessment authority

inputs/docs5-DOSSIER.md

Revision: None; SHA256: 95e2892cc0f8d87d8f46f8e19052315263e9f1ef4def0b2616e3c6df881b473b

proposed program; not accepted replacement identity

inputs/TRACERA-GAP-INVENTORY.csv

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: 374bb2a480178414caae0e46d754b7f8baac37002f42832297a77ff878bff4df

dated audit evidence; not current acceptance

inputs/TRACERA-GAP-ISSUES.md

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: 8e59a7dae096bfcf67af47c303ffc5a59d6758bed0236929b6144e0f7fd000b2

dated audit evidence; not current acceptance

inputs/TRACERA-BASELINE-PROMISES.csv

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: e6f07b9c7e427ed8af6720aa068881f8a853463c5576310685cc0e982a751327

dated audit evidence; not current acceptance

inputs/TRACERA-API-METHODS.csv

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: f86180032fa1ccd8f6c670b9dbb0cca8445c750a169caf22344476d97e4445ba

dated audit evidence; not current acceptance

inputs/TRACERA-HISTORICAL-VIEW-COVERAGE.csv

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: bd4a760f98def0aa11ac58eae7c39503bef3ba7cdf9d798070ef70685000fa92

dated audit evidence; not current acceptance

inputs/TRACERA-READINESS-AND-COMPLETION-PLAN.md

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: d4854f5a1f27e8f413f948bd8f4b66af2ff94f8a8249f498b53e7094c6dee634

dated audit evidence; not current acceptance

inputs/TRACERA-Q0-RUNTIME-QUALIFICATION.md

Revision: 3d02c5279ad30e5da61e037669955d37f6d8f7c7; SHA256: e109820af01aaf717afae850fcb106a135d7c8b507cd9da3a767c4fd716ad1a4

dated audit evidence; not current acceptance

inputs/source/README.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: 28e8ca9c7a08f030900322ffa85dc2bd3e3079bfa15cc8287ae326a9af7bc82b

source or historical contract; applicability unresolved

inputs/source/docs/ARCHITECTURE.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: cdb80df7ee843bbb47c8f8b836a9c4950a83fcdb2d6ad10fd1d7e9dbd926f296

source or historical contract; applicability unresolved

inputs/source/docs/FEATURE_INVENTORY.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: 203e2461df11f1cf6aae01bc8194cc5a0208c7edd55f09b98b845f836171a2c2

source or historical contract; applicability unresolved

inputs/source/docs/traceability.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: c4ff9d7360e1d66cf4a4efb18bcf649162cb7c3300c341d1e34ecc37d4a3782d

source or historical contract; applicability unresolved

inputs/source/docs/governance/policy/endpoint_traceability_map.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: ac6bf7b43c8c322ab78aec73db873b66eec7cda1923d2964b8a9477455554bb4

source or historical contract; applicability unresolved

inputs/source/docs/04-guides/mcp-cli-api-matrix.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: 95ed208b6908d210f3c31368fb4ece52aabd396b19b8c3a340d6e1e94dd1b271

source or historical contract; applicability unresolved

inputs/source/docs/WP-07-product-graph-design.md

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: f4555d8ee798f394ed69e8a0245b6e44ed3858bf881410e53928752da1dabcd7

source or historical contract; applicability unresolved

inputs/frontend-route-files.json

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: 8fc33f039435e6b990f5e441e62b35ba4683cafe8f33b9f7fa45bdbe11725169

bounded lexical census; not runtime coverage

inputs/frontend-api-candidates.json

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: 52334a4a05724dcfa12cc0b46292e0c112707ef9a576d2082c819916161fd5a6

bounded lexical census; not runtime coverage

inputs/unavailable-route-literals.json

Revision: ae68aea7febd772282606bf1e142d507316cfea0; SHA256: 26f85365fc50bde3c00b39d9b5c2c3a90c253532d2fa6faec5785190f9c12765

bounded lexical census; not runtime coverage

Integrity and publication

All projections derive from owner-records.json and snapshot.json. tools/render.py is the pinned evaluator-free renderer. views/build.json records input/output hashes and versions. No circular self-hash is claimed. Actual deployment, installed release, user feedback and acceptance remain independent gates.

{"project_commit": null, "project_pr": null, "registry_commit": null, "registry_pr": null, "safari": "NOT_OPENED", "code_pr": "https://github.com/KooshaPari/Tracera/pull/1157", "code_sha": "3fd3310fb98fdd2f9bca99eddd669f974fb1fb61", "code_state": "OPEN; UNSTABLE hosted checks; unmerged; not deployed", "registry_intent_pr": "https://github.com/KooshaPari/PhenoRegistry/pull/662", "registry_intent_sha": "22e8cdeb82f868faa805e884bdae63a9c715e0bc"}
